

ORCA – Watching Brief Daily Record Sheet

Site Code: <i>RSC'12</i>		Site Name: <i>KIRKDAL SHERIFF COURT</i>	
Site Personnel: <i>AMIN J LINDZAY</i>		Date: <i>20/2/12</i>	
Area Code: <i>TRENCH 1.</i>		Work Area NGR:	
Time onsite: <i>08:30</i>	Time offsite: <i>17:00</i>	point/line/area?	
Approx Area monitored: <i>1.65 x 5m</i>		Height:	
Approx DBGL: <i>C. 0.40m</i>		GPS type/accuracy:	
Work details/aims: <i>Monitoring of ground breaking and grading for disabled ramp construction.</i>		Method: <i>tarmaced surface cut with power saw, the surface then picked /chipped off. Jack hammer for SE and tarmac.</i>	
Plant details: <i>No plant - dug by hand by man team</i>		Contractor contact: <i>R.S. RENDALL</i>	

Description:

Deposits
Stratigraphy
Soils


Mottled tarmac surface - m in depth.

- Area to NE of existing steps two layers of tarmac, top layer 0.05m lower layer - 0.02m thick loose gravelly pot path surfacing. below. loose sub angular 10mm gravel comes down onto sub rounded pebble path foundation layer.

- Removal of steps revealed clay brick holed elec cable, robber cut

Sketch: *of Kirk Palace wall and and term both ends of wall, reprofiled.*


Location sketch
Sketch sections
GPS marker points
Annotation

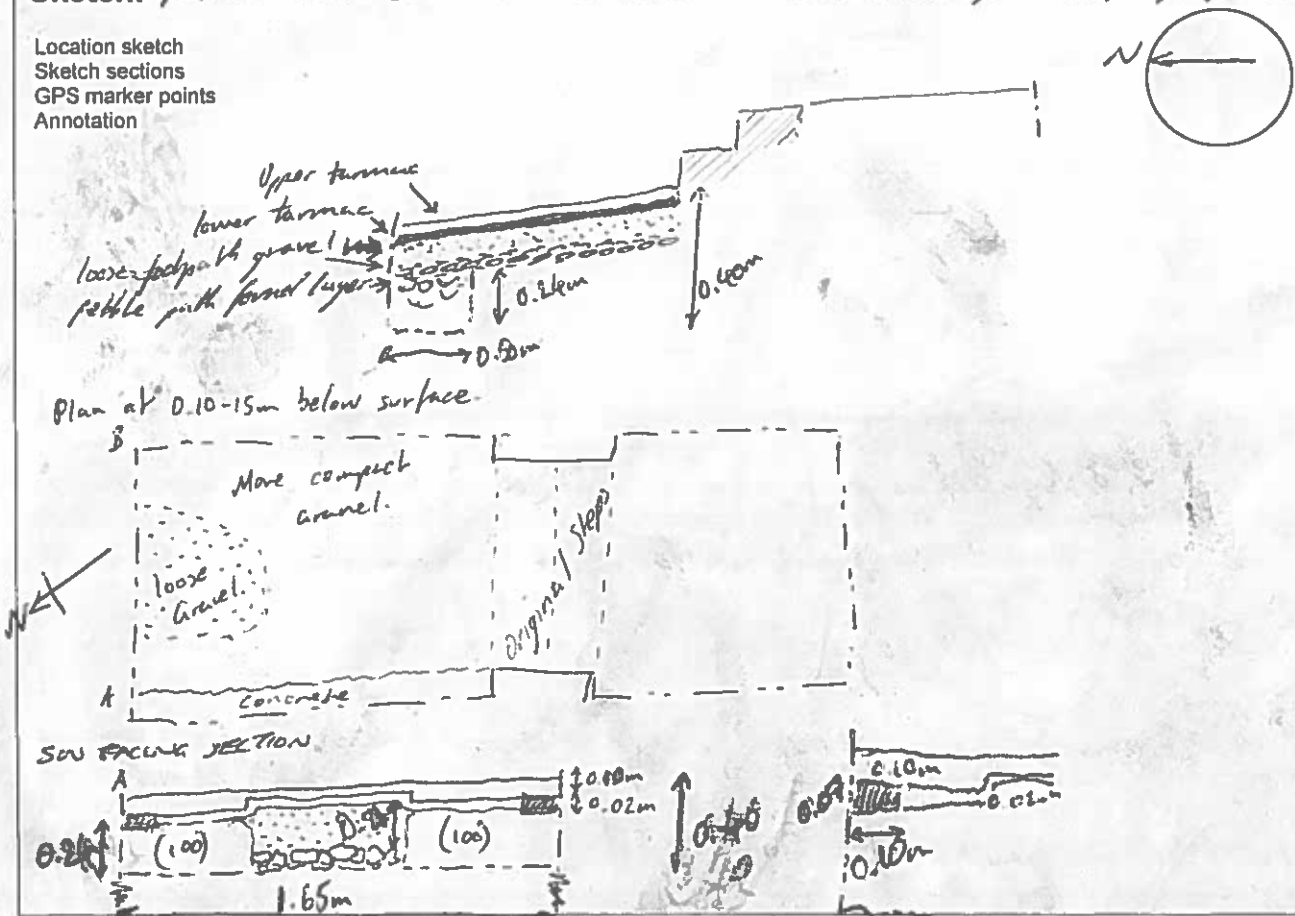

ORCA – Watching Brief Daily Record Sheet

Site Code: <i>KSC '12.</i>		Initials/date: <i>GJL. 20/2/12</i>	
Small finds: <i>Small bone frags.</i>		Ecofacts:	
<i>pettery clay pipe frags.</i>		Samples:	
SF No.	Type	Description	NGR
Additional comments/sketches:			

ORCA – Watching Brief Daily Record Sheet

Site Code: <i>RSC '12</i>		Site Name: <i>LIRK WALL SHERIFF COURT</i>	
Site Personnel: <i>G.J. LINDSAY</i>		Date: <i>22/2/12</i>	
Area Code:		Work Area NGR:	
Time onsite: <i>08:30</i>	Time offsite: <i>10:15</i>	point/line/area?	
Approx Area monitored: <i>c. 0.70m</i>		Height:	
Approx DBGL: <i>1.65 x 5m Area</i>		GPS type/accuracy:	
Work details/aims: <i>Monitoring removal of stone footing [107 & 108] and sealing of 101 & 102 with terram prior to concreting works.</i>		Method: <i>Covering of stonework by hand, removal of 107 & 108 by hand, sand spread with shovel & bucket.</i>	
Plant details: <i>No plant onsite all dug by hand.</i>		Contractor contact: <i>R.S. RENDALL</i>	
Description: Deposits Stratigraphy Soils <i>- Short monitoring of Removal of [107 & 108] stones and covering of wall heads 101 & 102 with terram and sand before construction gravel was laid.</i>			
Sketch: Location sketch Sketch sections GPS marker points Annotation 			

ORCA – Watching Brief Daily Record Sheet

Site Code: KSC 12		Initials/date: GJL 22/2/12	
Small finds:		Ecofacts:	Samples:
SF No.	Type	Description	NGR
Additional comments/sketches:			
